



# Barron Park

## CIP Project Update

### Strategic Plan 2015 Goal:

*Goal 3) Promote the Visual Image of El Paso*

*Goal 4) Enhance El Paso's Quality of Life through Recreational, Cultural and Educational Environments*

**August 4, 2015**

*"Delivering Outstanding Services"*



# Barron Park

## Project Timelines

- **City Council Award: November 12, 2013**
- **Notice to proceed issued: February 3, 2014**
- **Original substantial completion: July 4, 2014**
- **Original final completion: August 2, 2014**
- **Amount of days issued due to change orders: 160 days**
- **Adjusted substantial completion date: December 10, 2014**
- **Adjusted final completion: January 10, 2015**
- **Engineering's forecast for completion and open to the public: September 2015**



## **Barron Park**

**Project Manager:** Julian Rodriguez

**District:** 4

**Approved Budget:** \$1,500,000

**Source(s) of Funding:** 2012 Quality of Life

**Council Approval of Construction:** November 12, 2013


**Contractor's Project Manager:** Steve Allen

**Formal Notice to Proceed:** February 3, 2014



# Barron Park

## Site Location

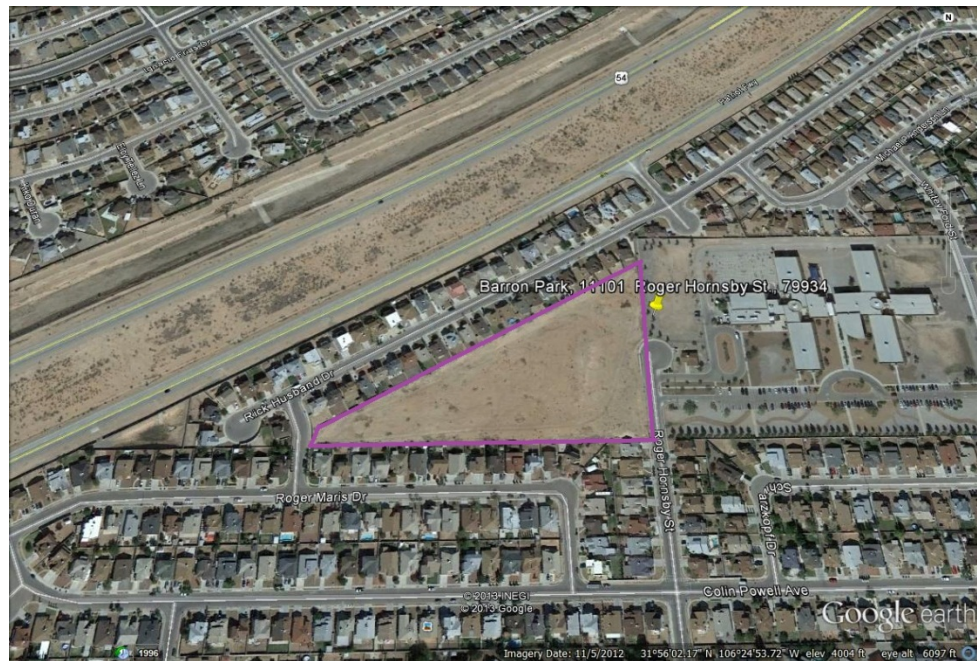

*"Delivering Outstanding Services"*



# Barron Park

## Kiosk and picnic tables



*"Delivering Outstanding Services"*





# Barron Park

## Walkways and park lighting



*"Delivering Outstanding Services"*



# Barron Park

## Sod Area



*"Delivering Outstanding Services"*



# Barron Park

## Basketball Courts





*"Delivering Outstanding Services"*





# Barron Park

## Work in Progress

Project Element	Task Description	Status
Electrical	Walkway and courts lighting	COMPLETE 
Furniture	Benches, trash receptacles, bike racks and picnic tables	COMPLETE 
Structures	Kiosk and play ground area canopies	COMPLETE 
Irrigation	Main line, laterals and sprinkler heads	COMPLETE 
Courts	Basketball and football courts	95% complete
Landscape	Tree and shrub planting	80% complete

*"Delivering Outstanding Services"*



# Barron Park

## Work in Progress

Project Element	Task Description	Status
Sod	Sod area	90% complete
Pedestrian elements	Walkways and plaza area	95% complete
Ground cover	Rock mulch	80% complete
Pump house	Irrigation pump installation	20% complete, to be finish once planting is completed
Striping	Parking spaces and ADA access and signage	To be completed after final clean up

*"Delivering Outstanding Services"*



# Barron Park

## Threats to Project Completion

- Tree and plant availability




## Barron Park

**Open to the Public:** Fall of 2015

**Notice to Proceed:** February 13, 2014

**Council Award:** November 12, 2013





# Barron Park

End of Presentation

## Questions & Comments

*"Delivering Outstanding Services"*
