



CIP Project Update

San Jacinto Plaza



"Delivering Outstanding Services"

August 4, 2015



San Jacinto Plaza

2015 Strategic Plan:

Goal 3) Promote the Visual Image of El Paso

Goal 4) Enhance El Paso's Quality of Life through Recreational, Cultural and Educational Environments



San Jacinto Plaza

Project Timelines

- **City Council Award: January 14, 2014**
- **Notice to proceed issued: February 17, 2014**
- **Original substantial completion: January 13, 2015**
- **Original final completion: February 12, 2015**
- **Amount of days issued due to change orders: 128 days**
- **Adjusted substantial completion date: May 21, 2015**
- **Adjusted final completion: June 21, 2015**



San Jacinto Plaza

Project Manager: Gilbert Guerrero

District: 8

Approved Budget: \$6,000,000

Source(s) of Funding: Quality of Life

Council Approval of Construction: January 14, 2014


Contractor's Project Manager: Eddie Linss

Formal Notice to Proceed: February 17, 2014



San Jacinto Plaza

Site Plan

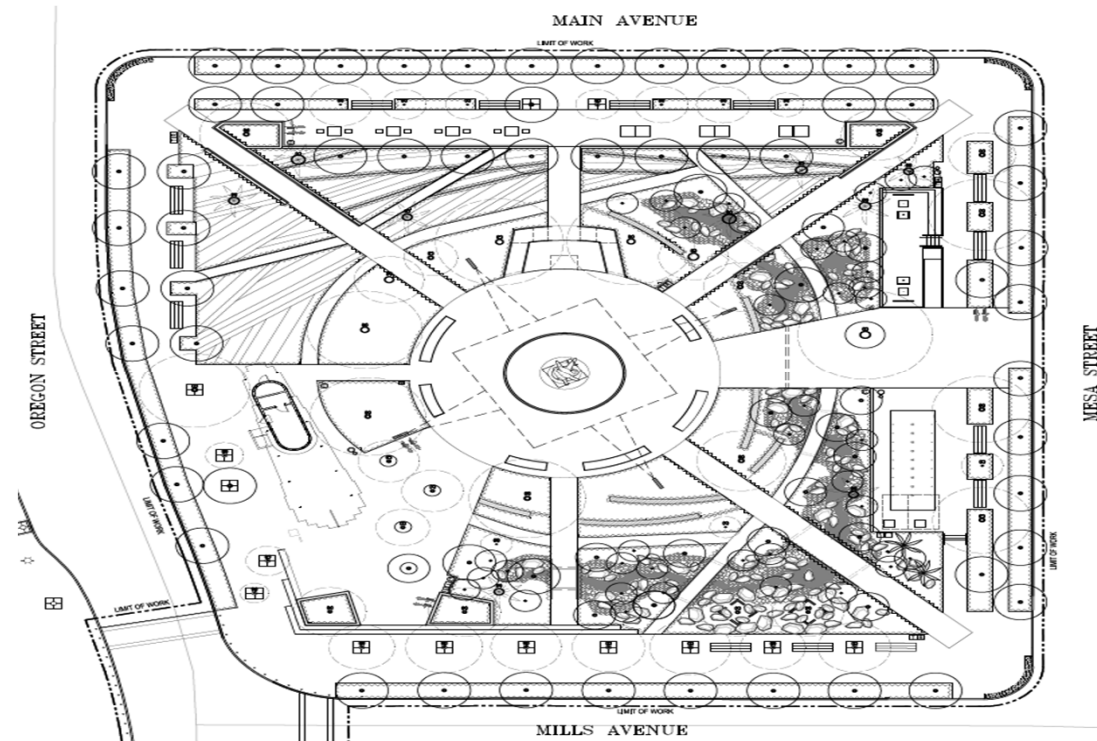


"Delivering Outstanding Services"



San Jacinto Plaza

Arroyos & Pedestrian Bridges

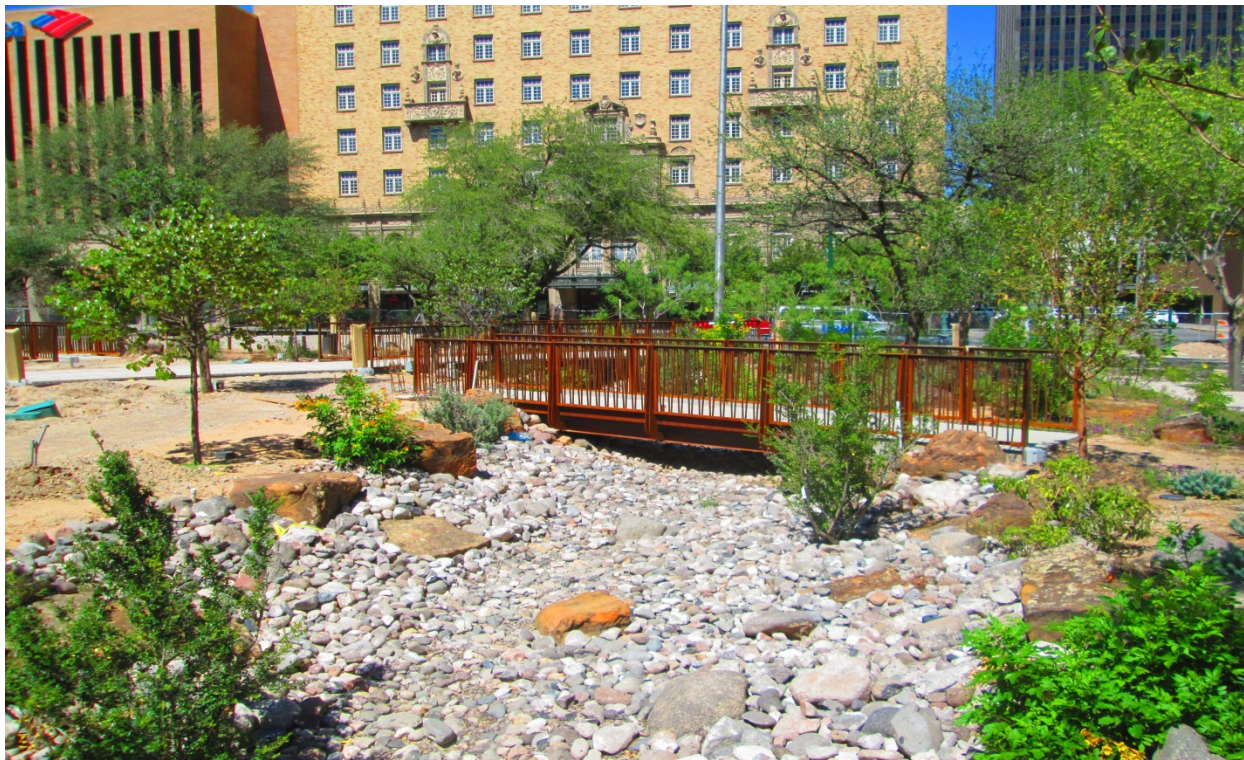

"Delivering Outstanding Services"



San Jacinto Plaza

Splash Pad



"Delivering Outstanding Services"



San Jacinto Plaza

Game Tables and Benches



"Delivering Outstanding Services"



San Jacinto Plaza

Concrete Columns









"Delivering Outstanding Services"



San Jacinto Plaza

Work in Progress

Project Element	Task Description	Status
Arroyos	Landscape and rock ground cover	COMPLETE 
Sedimentary Walls	Cast in place color concrete	COMPLETE 
Pedestrian Bridges	Steel and concrete installation	COMPLETE 
Concrete Columns	Steel, foundations and concrete installation	COMPLETE 
Electrical Panels	Relocation of above ground electrical	COMPLETE 
Landscape	Perimeter of Main, Mesa & Mills	COMPLETE 

"Delivering Outstanding Services"



San Jacinto Plaza

Work in Progress

Project Element	Task Description	Status
Steel Cables	35 of 36 cables stored at EPIA warehouse. Contractor in process of ordering damaged cable	Pending delivery schedule of damaged cable
Café Building	Concessionaire building	90% complete
Site electrical	Installation of wire, outlets, lighting, and control panels	85% complete
Steel Canopy	Repair of canopy steel members	80% complete
Brick Pavers	Installation of paver walking paths	80% complete
Resysta Wood	Installation of resysta wood along walking paths	Start install after canopy is hung

"Delivering Outstanding Services"



San Jacinto Plaza

Work in Progress

Project Element	Task Description	Status
Pavers under canopy & Oregon St.	Install decorative pavers under canopy area	To be started once canopy is hung
Landscape under canopy & Oregon St.	Install Irrigation, trees and shrubs under canopy area	To be started once canopy is hung
Site Furnishings	Install tables and chairs under canopy area	To be started once canopy is hung
Reflective pool & Lagartos art	Specialty tiles and art piece installation	To be started once canopy is hung

"Delivering Outstanding Services"



San Jacinto Plaza

Threats to Project Completion

- **Damaged cable will have to be manufactured, shipped and clear customs**



San Jacinto Plaza

Open to the Public: Holidays 2015

Notice to Proceed: February 17, 2014

Council Award: January 14, 2014



"Delivering Outstanding Services"



San Jacinto Plaza

End of Presentation

Questions & Comments

"Delivering Outstanding Services"
