




# Weekly Project Update

## Pedestrian Pathway

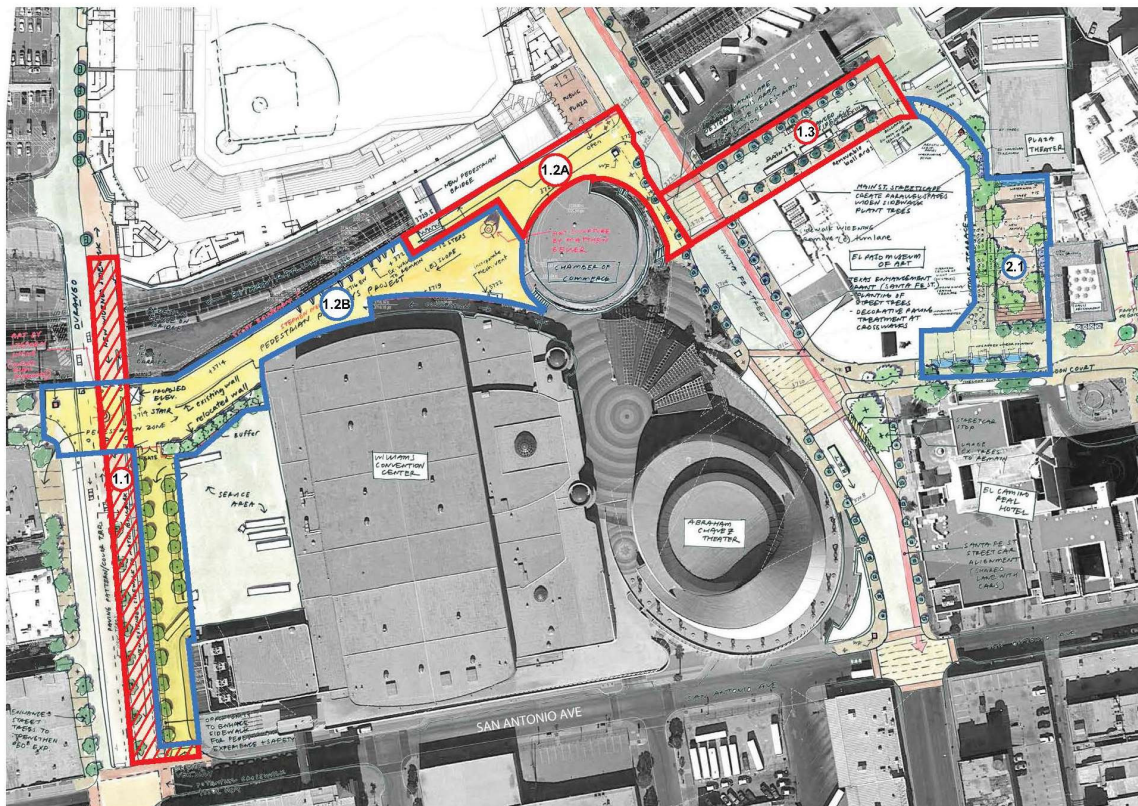

**PHASE 1**

- 1.1** DURANGO STREET ENHANCEMENTS FROM FRANKLIN ST TO SAN ANTONIO ST. 22,000 SF
- 1.2A** PEDESTRIAN PATHWAYS PROJECT - EAST AREA 17,550 SF
- 1.3** MAIN STREET ENHANCEMENTS, INTERSECTION IMPROVEMENTS AT SANTA FE ST 23,150 SF

**PHASE 2**

- 1.2B** PEDESTRIAN PATHWAYS PROJECT - WEST AREA 57,450 SF
- 2.1** ARTS FESTIVAL PLAZA 39,700 SF



## Pedestrian Pathway

**Project Manager**   Gilbert Guerrero

**District**   8

**Approved Budget**   \$6,500,000

**Source(s) of Funding**   2012 Quality of Life Bonds

**Council Approval**   5/1/13 (City Site Work & Parkway Structures)

**Notice to Proceed**   November 13, 2013

---





# Pedestrian Pathway, Phase 2.1 Arts Plaza

## Construction



Rough grading complete, underground conduits to follow



# Pedestrian Pathway, Phase 1.3 Main St.

## Construction



Main Street 95% complete



# Pedestrian Pathway, Phase 1.2A

## Construction



Planters along Santa Fe Street



# Pedestrian Pathway, Phase 1.2 B

## Construction




Underground conduits complete, final grading to follow

S E R V I C E   S O L U T I O N S   S U C C E S S



# Pedestrian Pathway, Phase 1.2 B

Rendering





# Pedestrian Pathway, Phase 1.1 Durango Bridge

Construction



95% complete, pending fence replacement



# Pedestrian Pathway

## Work In Process and Remaining for Completion

### Phase 2.1 (Arts Plaza)

- Installing underground utilities
- Foundations for planters
- Start concrete pavement January 10, 2015
- Complete phase 2.1. February 27, 2015

### Phase 1.3 (Main)

- Pending final electrical connections. Electrical source located in phase 1.2A

### Phase 1.2A (Chamber of Commerce)

- Underground utilities complete
- Planters 85% complete
- Concrete paving, to be started December 29, 2014
- Complete Phase 1.2A. January 30, 2015



# Pedestrian Pathway

## Work In Process and Remaining for Completion

### Phase 1.2B (Convention Center)

- Underground utilities 90% complete
- Foundations for public art, canopy and planters 100% complete
- Starting final grading
- Start concrete placement November 24, 2014
- Install public art November 18, 2014
- Complete phase 1.2B. January 30, 2015

### Phase 1.1 (Durango Bridge)

- Pending replacement of existing fence on Durango Bridge
- To be Completed January 15, 2015



# Pedestrian Pathway

## Threats to Project Completion

- Freezing weather, rain/snow



# Pedestrian Pathway

## Public Outreach and Stakeholder Engagement

- **Ground breaking**  
November 4, 2013
- **Construction Weekly Meetings**



# Pedestrian Pathway


Date	Change Order	Budget Impact
1/8/14	Install electrical conduit and pull boxes for future tree string lights on Main street (Phase 1.3)	\$8,779.00
2/28/14	Remove existing light poles at center of sidewalk on Main Street, Install foundations and conduit for new street illumination, Modify ramp at Santa Fe & Main in order to comply with ADA, Remove and dispose of thicken asphalt pavement. (Phase 1.3)	\$25,352.00
5/22/14	Repair existing leaking water line, install silt fence and rock construction exit, relocate water line and spout, remove existing traffic signal foundation, increase size of tree grates to 6'x6' (Phase 1.2A)	\$8,761.00
11/23/14	Install drill piers at mechanical room, install larger diameter pipes for high pressure water lines, install exhaust fan in mechanical room, and install larger backflow preventer (Phase 1.2A)	\$24,969.00
10/2/14	Remove and dispose of existing thick concrete sections (Phase 1.2B)	\$ 8,000.00
10/28/14	Remove and dispose of a portion of existing concrete planter walls, remove large branches from exiting trees to allow equipment to install drill piers at mechanical room.	\$ 3,639.00



# Pedestrian Pathway

**Project Start Date: November 13, 2013**

**Currently Projected Completion Date: February 27, 2015**





## Pedestrian Pathway

### Project Management Team

<b>City of El Paso's Project Manager</b>	Gilbert Guerrero Engineering and Construction Management
<b>Contractor's Project Manager</b>	Arturo Fuentes JAR Concrete, Inc.

Engineering and Construction Management staff is meeting weekly with the contractors to ensure that the project is completed on schedule.
