

Project Update

Great Streets and Corridor Plan

Strategic Plan 2015 Goal:

- 7) Enhance and Sustain El Paso's Infrastructure Network <u>Strategy</u>:
 - 7.4 Continue the strategic investment in city facilities and technology
 - 7.5 Set one standard for infrastructure across the city





Project Manager Justin Bass

District All Districts

Approved Budget \$108,830.00

Total Expended \$16,015.69

Source(s) of TxDOT

Funding City Match (20% of total cost)

Council Approval August 12, 2014

of Resolution

Notice to Proceed November 10, 2014



Project Management Team

City of El Paso's Justin Bass

Project Manager | Engineering and Construction Management

URS Keith Dewey

Project Manager | Senior Planner, AICP



What are Great Streets?

- Streets for Everyone, No Matter Who They Are or How They Travel
- Safe, Comfortable, Convenient
- Accommodate All Users and Modes
- Context Sensitive
- Have Appropriate, Attractive and Abundant Landscaping
- Can Incorporate Green/Sustainable Elements



Typical Great Streets





Typical Great Streets





Great & Not-So-Great Streets











El Paso Example





El Paso Example




El Paso Example





Project Limits: Citywide

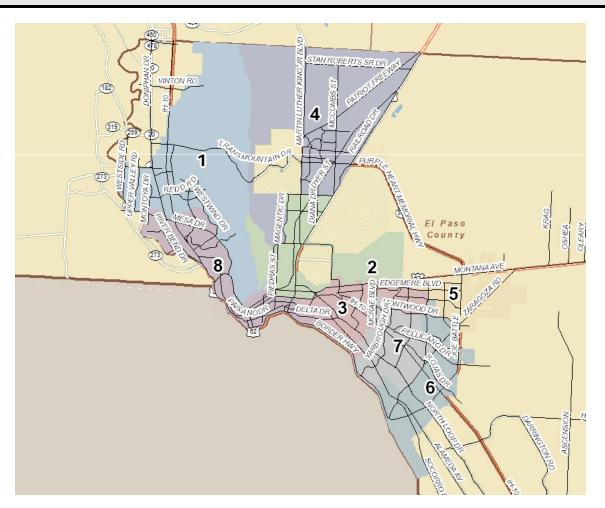



Public Outreach and Community Engagement

- Public Meetings
 - December 18, 2014 Downtown (City Hall)
 - January 14, 2015 Pebble Hills Regional Command
 - February 12, 2015 Mission Valley Regional Command
- Additional monthly meetings required through duration of plan creation.
 - March 19, 2015 Northeast Regional Command 6pm
 - April 16, 2015 Westside Regional Command 6pm



Plan Composition – Scope of Work

- Great Streets Policy
 - → Overall Policy Statement
 - **→** Goals & Objectives
- Design Standards
 - **→** General Design Standards
 - → New Cross-Sections/Guidelines
- Implementation Plan
 - → Identification of which roadways/corridors funded, designed, or in progress meet policy and design standards
- Thoroughfare Plan
 - → Review and reclassification of some roadways on MTP
 - → Map to identify before/after roadway reclassifications



Original Consultant Project Completion Date: May 15, 2015 Current Consultant Project Completion Date: May 15, 2015

